



**RWinvest**

# **BRIDGEWATER POINT**

Construction Update  
July 2018

# **Bridgewater Point**

## **Bridgewater St, Manchester, M3 4NH**

### **Works Complete**

#### **Block A**

- The reception area is 95% complete; the reception counter is installed and there are still minor decoration works to be completed.
- Level 1 to 4 units are 99% complete with final snagging and cleaning being carried out.
- Level 5 units are 85% complete with all kitchens and sanitary ware installed.
- Mechanical and electrical second fix works are to be completed, as well as second fix joinery on level 5.
- Corridor ceilings are all installed with decoration well progressed and the floor coverings have begun to be installed through communal areas.

#### **Works Scheduled Block A**

Final snagging and cleaning to follow.

#### **Block B**

- Floors 1 and 2 are 90% complete with floor coverings complete and programmed works for electrical testing to commence along with water tests.
- Floors 3 to 4 are 85% complete with floor coverings progressing and final stages of joinery works underway.
- Floors 5 to 6 are 75% completed with mechanical and electrical second fix works being carried out along with second fix joinery. Decoration is continuing throughout.
- Floors 7 to 8 are 70% complete with final kitchens been installed and remaining plots due to be mist coated.

#### **External**

The external podium works has steelwork, metal deck and concrete poured with other works to the external areas commencing shortly.


If you need any further information in the meantime, please call us at the following offices:

Liverpool +44 (0)151 808 1250

London +44 (0)207 100 4141





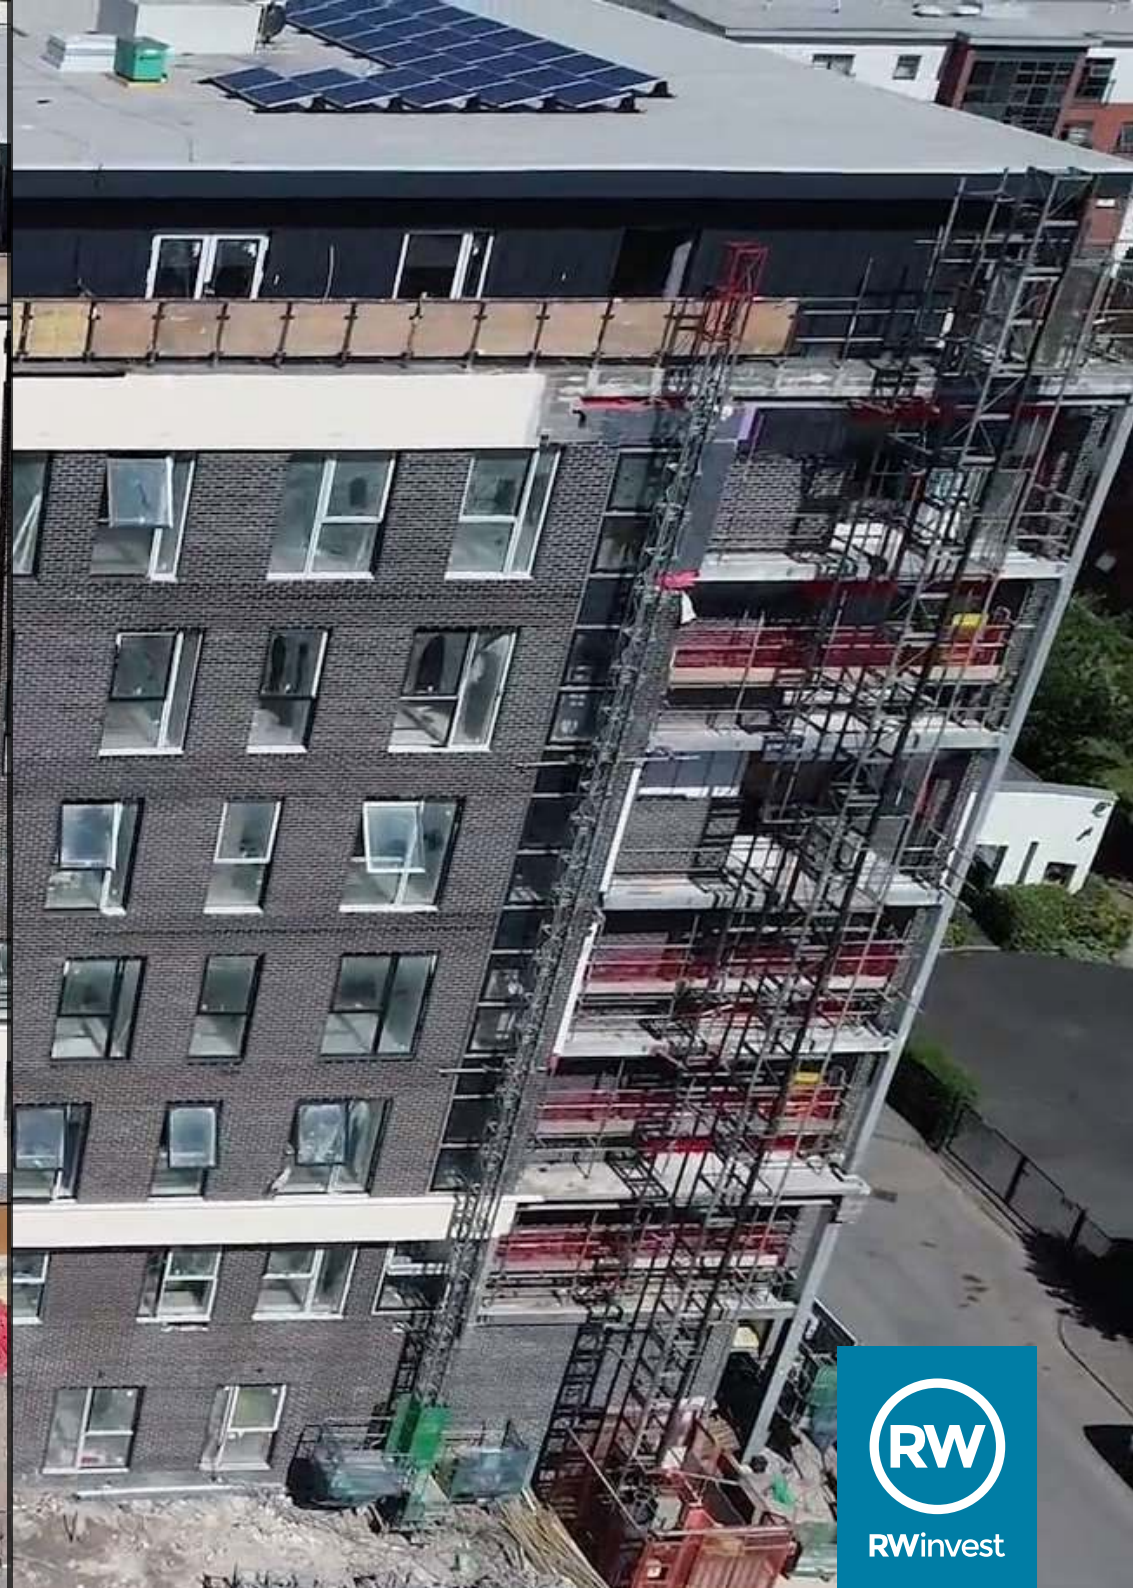

RWinvest





RWinvest
