



RWinvest



FABRIC DISTRICT RESIDENCE

Construction Update
March 2019

Fabric District Residence 33 Devon Street, L3 8HA

Works are progressing well at Fabric District Residence on Devon Street, Liverpool. Structural steel, first phase rib deck and 40% of the substructure masonry works are complete. In the next construction period. Concrete floor will be poured to allow for the joint installation and concrete stairs will be installed among many other pivotal construction activities.

Works Progressed


- Structural steel is complete.
- First phase rib deck complete.
- Concrete to phase one on the first floor has been poured.
- Completed approximately 40% of the substructure masonry works.
- Commenced formation of the ground floor slab.
- Appointed the façade contractor.
- Appointment of fit out contractors is in latter stages.

Works Scheduled

- Completion of second phase rib deck to the first floor.
- Arrival of timber joists to the upper floors.
- Scaffolders to commence second phase to provide edge protection for the rib deck installation team.
- Concrete floor will be poured for phase two allowing access for the joist installation.
- Concrete stairs installation.
- Commence the envelope works to the nine-story portion of the building.
- Commence timber joists to phase two.

If you need any further information in the meantime, please call us at the following offices:

Liverpool +44 (0)151 808 1250
London +44 (0)207 100 4141

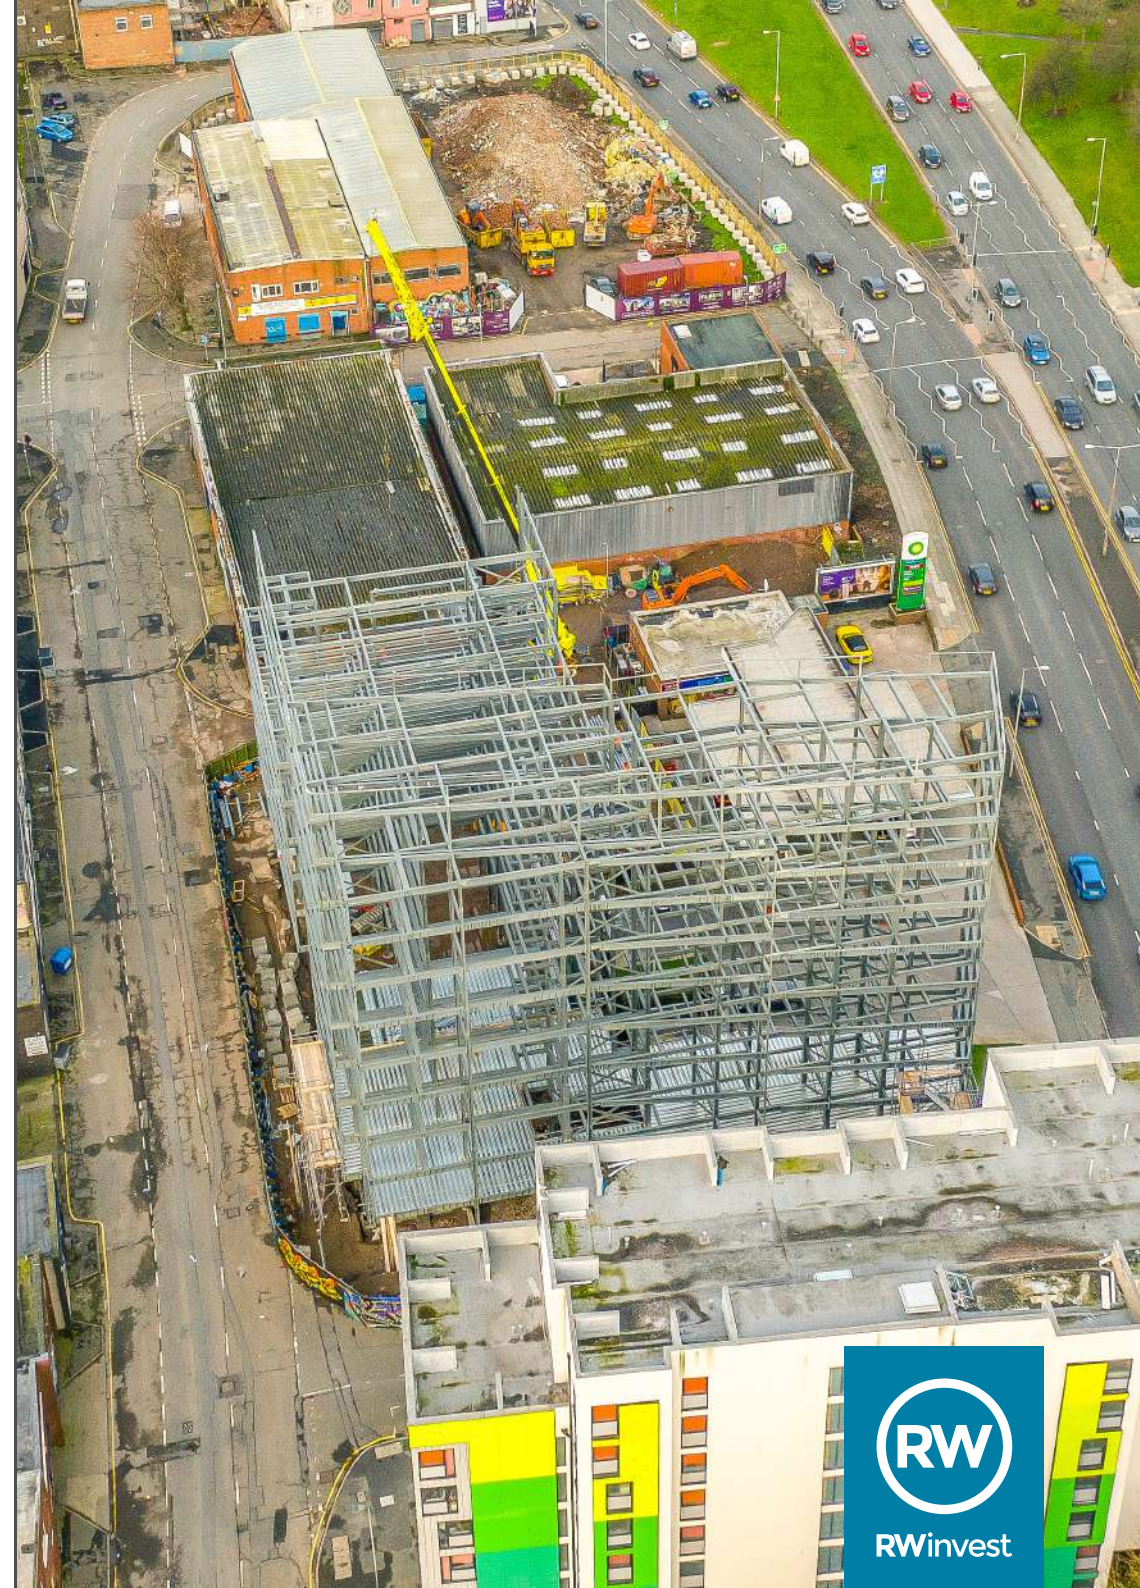



RWinvest
