



RWinvest



**HALO**  
Construction Update  
January 2018

# Halo School Street, New Mount Street And Ludgate Street, Ancoats, Manchester, M4 4AS

## What's New?

Significant progress is visible on-site this month as works are now entering week 40 of the 82-week programme. The basement is now complete and the concrete frame has been extended to the ground floor level.

Metal frame and flooring on the first-floor level is now 80% complete and brickwork infill to the ground floor has this month reached completion.

## The Schedule


Work on the steel frame erection now continues along with the continuation of works to frame panels and concrete infill to piles.

If you need any further information in the meantime, please call us at the following offices:

Liverpool +44 (0)151 958 1254

London +44 (0)207 100 4141



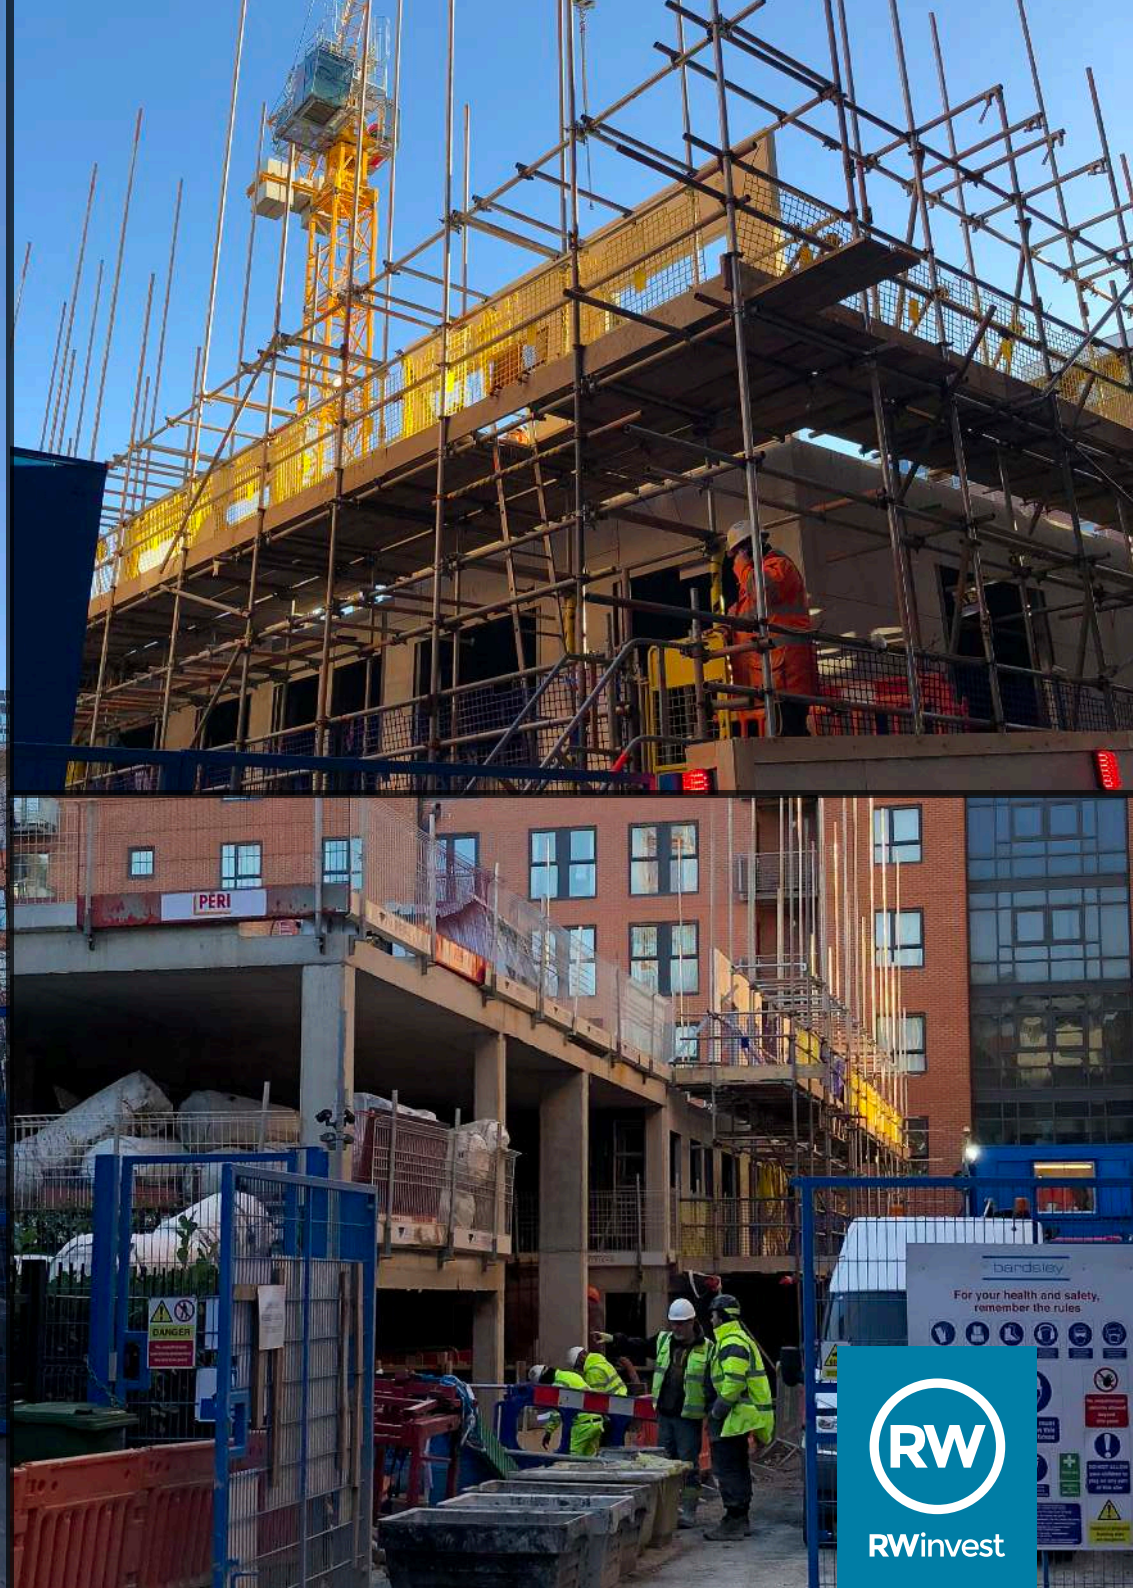

RWinvest
