



Central Park Construction Update

SEPTEMBER
2023

September 2023

Estimated Completion date: Q1 2025

Significant progress has been made at Central Park recently as site clearance continues in preparation for onsite piling. These works included breaking ground, as well as the preparation and construction of the piling mat.

The jaw crusher was also delivered recently as part of these preparations, which will enable the commencement of onsite piling over the coming weeks.

Summary of Works Progressed

- Preparation of the piling mat and site clearance.
- Breaking ground in preparation for piling mat.
- Construction of the piling mat in preparation for the piling rig.
- Delivery of the jaw crusher for installation of the piling mat.

Works Anticipated

- Commencement of piling.



Central Park - Breaking Ground



Central Park - Breaking Ground



Central Park - Plant in Operation




Central Park - Plant in Operation



Central Park - Site Activity




Central Park - Piling Mat Commenced

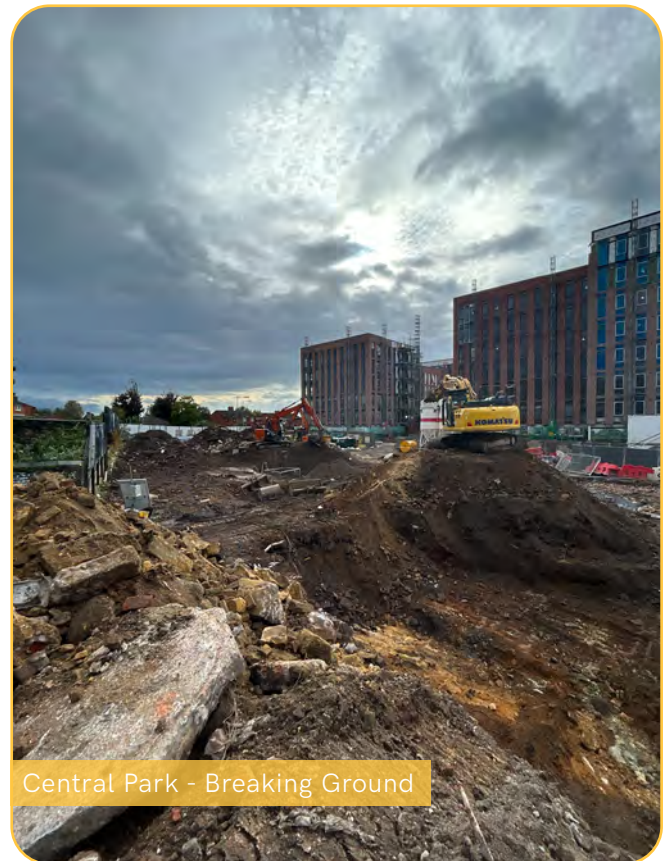

Central Park - Breaking Ground



Central Park - Construction of Piling Mat

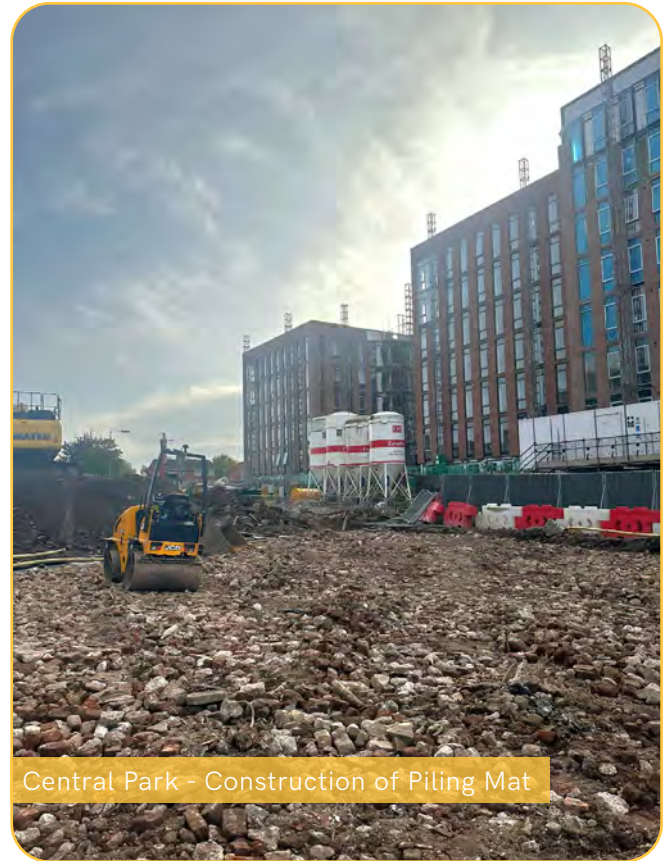

Central Park - Construction of Piling Mat



Central Park - Delivery of Jaw Crusher



Central Park - Piling Mat Prepared
